


TAMU VOAL: MS Project Gantt Chart

Here is an example of some activities with precedence and a milestone to represent a presentation:

	 Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		Activity 1	4 days	Sun 9/8/24	Wed 9/11/24	
2		Activity 2	3 days	Thu 9/12/24	Mon 9/16/24	1
3		Activity 3	8 days	Wed 9/11/24	Fri 9/20/24	
4		Activity 4	2 days	Mon 9/23/24	Tue 9/24/24	2,3
5		Presentation 1	0 days	Wed 9/25/24	Wed 9/25/24	

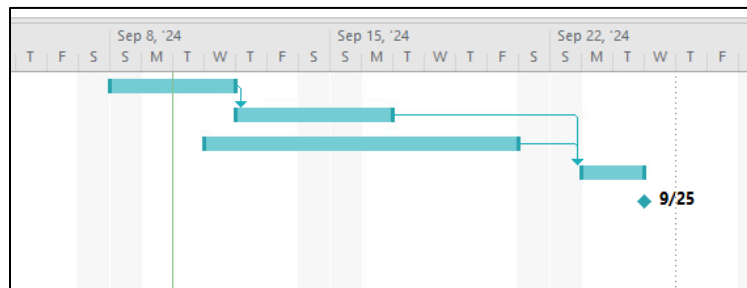


To make the Gantt workbook into something that you can insert into your presentation, there are a few tweaks that need to be made.

First, we would like to see activity/task names on top of the bars **on the chart**. To do this, select all tasks by pressing the region in the top left of the spreadsheet part:




	 Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		Activity 1	4 days	Sun 9/8/24	Wed 9/11/24	
2		Activity 2	3 days	Thu 9/12/24	Mon 9/16/24	1
3		Activity 3	8 days	Wed 9/11/24	Fri 9/20/24	
4		Activity 4	2 days	Mon 9/23/24	Tue 9/24/24	2,3
5		Presentation 1	0 days	Wed 9/25/24	Wed 9/25/24	


Go to the “Gantt Chart Format” tab and select “Format” > “Bar”.




Enter “Name” into the “Top” field:

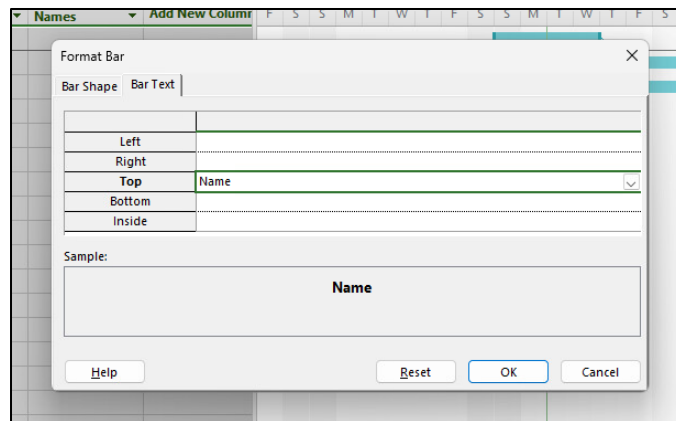


The bar section should now look like this:

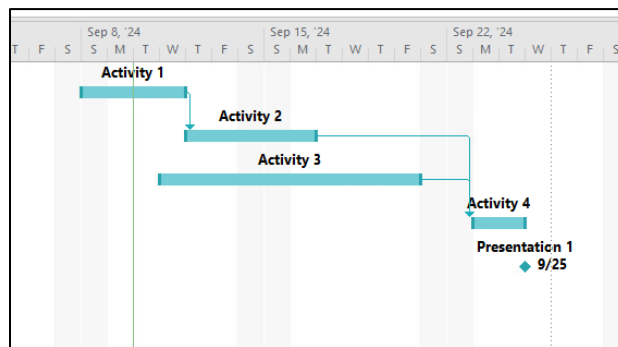


The default print view is not what we want, so go to “Page Setup”:

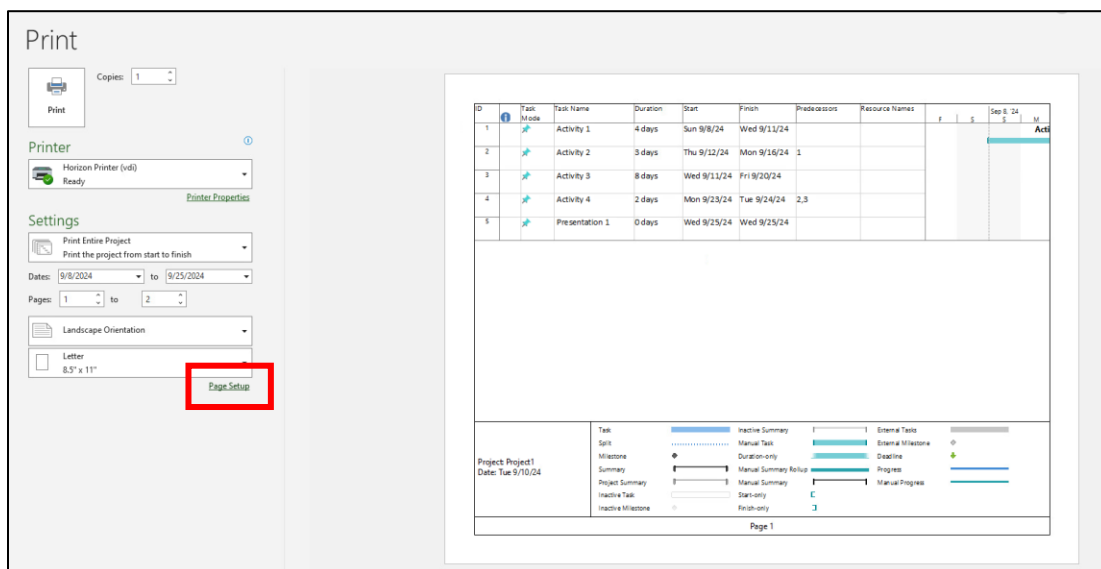

Go to the “Legend” tab, set “Legend on:” to “None”. Now, it won’t print with the legend. To make sure it prints without the tabular data on the left, drag the edge of the bar section with your cursor to cover the tabular region. After dragging the edge to the left, your workspace should look something like this:

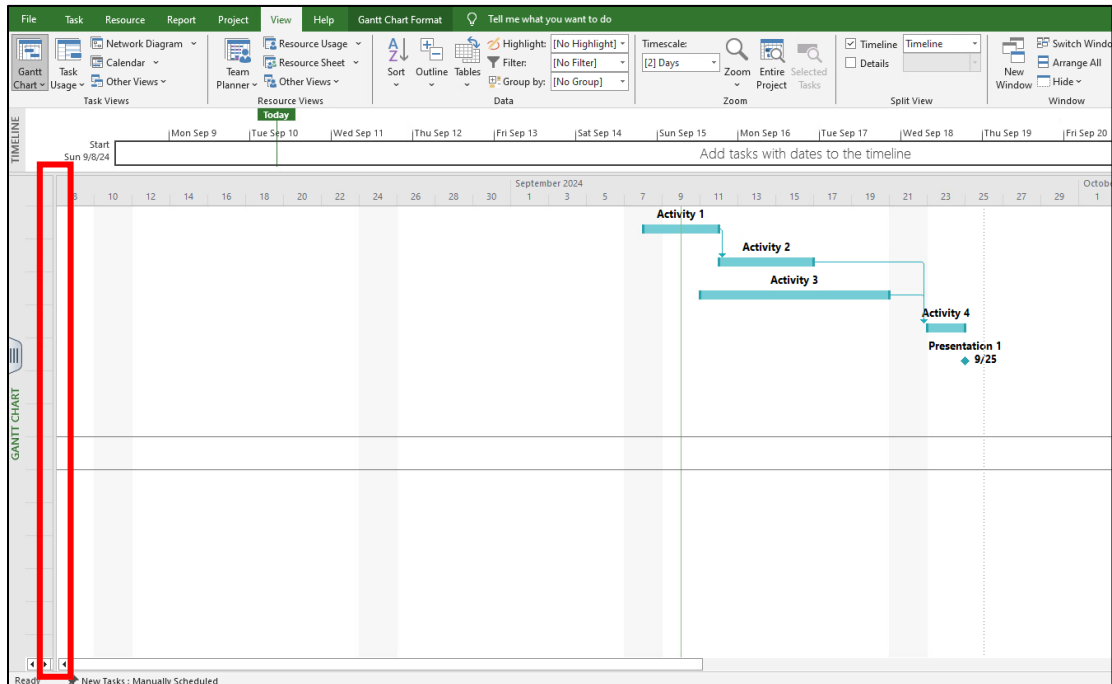

Now, when you go into the print tab, set it to “Print Custom Dates and Pages” and enter the timeframe you need. Once set, you may need to go back into the worksheet and tweak the zoom to ensure that everything is captured.

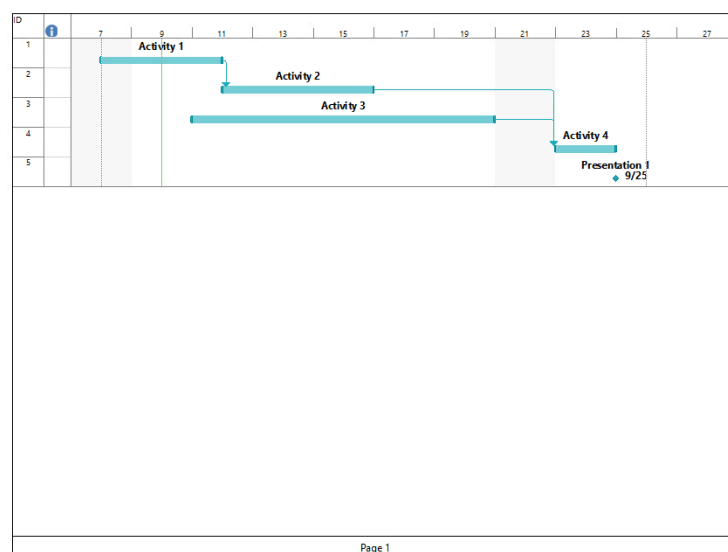

From here, you’ll be able to either export or screenshot and insert your Gantt chart into your slides.

There are many other functions/features available in MS Project such as task completion percentage, summary tasks to describe task clusters (useful for organizing work by phase as we progress into the semester), and resource assignments (for assigning people on your team to tasks). All that's required is what's mentioned in the checklist, however, don't let the bare minimum requirements stop you from enhancing your teams project plan.

Please reach out to one of the TA's if you're having difficulty with MS Project or figuring out how to display your Gantt Chart in your slides.
